Providence School Building Committee

Capital School Projects Update

December 17, 2024








Project Update

School Name	Project Budget (Based on Amendments to 2019 & 2022 MOA's)	Student Capacity	Completion Date			
Construction						
D'Abate Elementary School	\$22,000,000	365	Occupied			
Frank Spaziano Elementary School	\$44,000,000	684	Occupied			
George West Elementary School	\$525,000	601	Completed			
Pleasant View Elementary School	\$18,109,132	418	Fall 2024			
Esek Hopkins Middle School	\$450,000	595	Completed			
Nathanael Greene Middle School	\$2,000,000	772	Completed			
Classical High School	\$40,278,711	1113	Fall 2025			
Hope High School – Phase 1 completed	\$18,000,000	18,000,000 1135 Pha				
Narducci Learning Center	\$30,500,000	700	Occupied			
Pre-Construction (Phase 2)						
Frank Spaziano Middle School	\$34,500,000	300	Fall 2025			
Harry Kizirian Prek – 8	\$55,253,171	729	Summer 2026			
Fogarty Prek-8	\$56,575,600	729	Summer 2026			
Phase III - Development						
Messer/WBroadway Prek-8	\$62,500,000	972 (est)	Summer 2027 (est)			
Lima/Stuart Prek-8	\$62,500,000	972 (est)	Summer 2027 (est)			
Mt. Pleasant Early Career and College Academy	\$110,000,000	1000 (est)	Summer 2027 (est)			
RFK PK-8						







Project Update

					Provid	lence Pub	lic School	s RIDE Stag	je ll 2024					
Projects									M	ajor Scopes of	Work			
School	Size	Grade Levels	#of Classroom s per Grade	# of Students	Budget	New HVAC	Building Envelope (Roof, Windows, etc.)	New Secure Entrance, Security Improvements, Energy Efficiency	ADA Improvements	Restroom Renovations	Educational Enhancements	Interior Finishes	Site Improvements	Fire Marshal Deficiencies
Carnevale														
Delsesto														
Vartan														
New Build @ MLK**														
Hope														
Greene *														
New Build @ Kennedy **														
Roger Williams*														
-														
* Includes a new 10,000 Sq.I		_						_			_		_	
** According to RIDE Guideli		Phase 1 projects are under review and additional												
	Phase 4 projects are under review and additional													
School														
Central		updates will be provided at future meetings.												
Leviton														
Bishop														
Alvarez														
Bailey														
PCTA														
E-Cubed														
JSEC														
Young & Woods														
Classical														
Total Revolving Fund														

Groundbreakings and Ribbon Cuttings



Gymnasium, full kitchen, cafeteria and media center

DOWNES

Building Futures, Inspiring Learning A New Era for Harry Kizirian



Learning commons, breakout rooms for group

activities and teacher planning

Classical High School

PROJECT SPOTLIGHT



Completion Date: Fall 2024

Project Budget: \$40,278,71



Classical High, one of the highest performing high school's in the state, has been renovated with a project budget of \$40,278,711. In a multi-phased project, 8 months ahead of schedule, this building has been transformed into an incredible state of the art facility where students are equipped to get the most our of their learning. This school will be supporting 678, 9-12th grade students who have seen the progression of renovations over the past few years and have continuously commented on the stark difference.

CLASSICAL HIGH SCHOOL:

Building a Future of Innovation, Learning, and Community






CITY OF PROVIDENCE






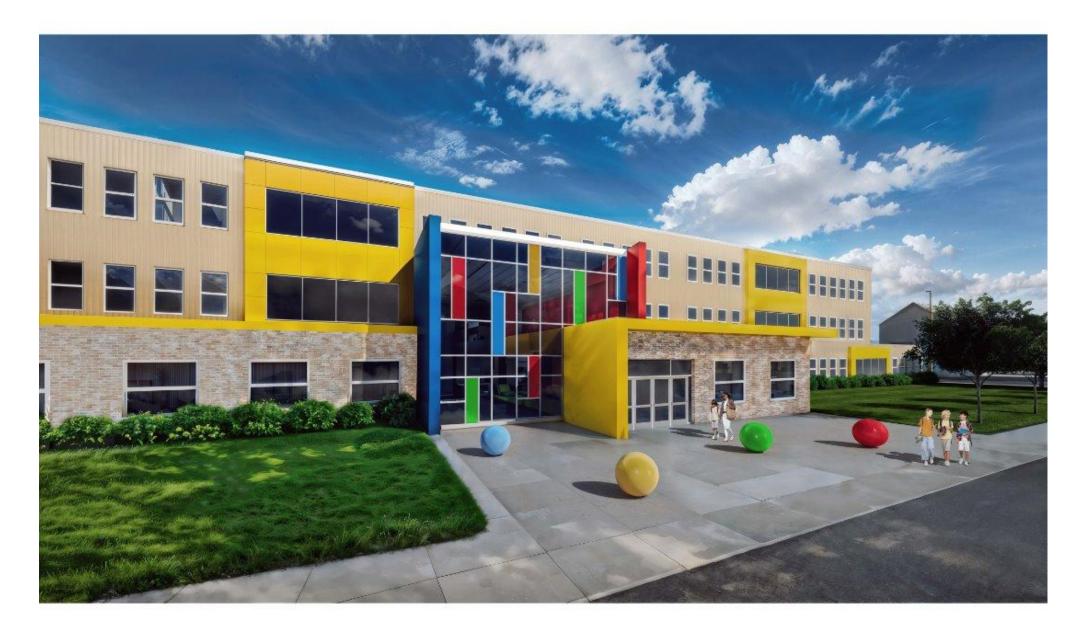




MARY E. FOGARTY ELEMENTARY SCHOOL PRE K - GRADE 5 | 3 TRACK GRADE 6 - GRADE 8 | 4 TRACK



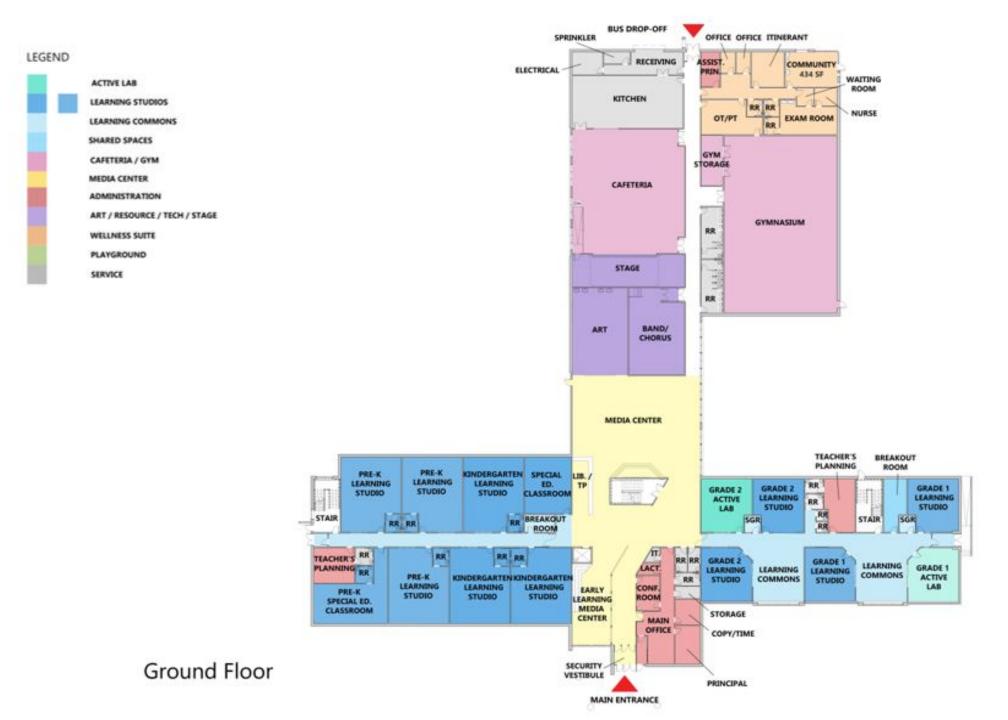


LEGEND

ACTIVE LAB LEARNING STUDIOS LEARNING COMMONS SHARED SPACES CAFETERIA / GYM MEDIA CENTER ADMINISTRATION ART / RESOURCE / TECH / STAGE WELLNESS SUITE PLAYGROUND SERVICE

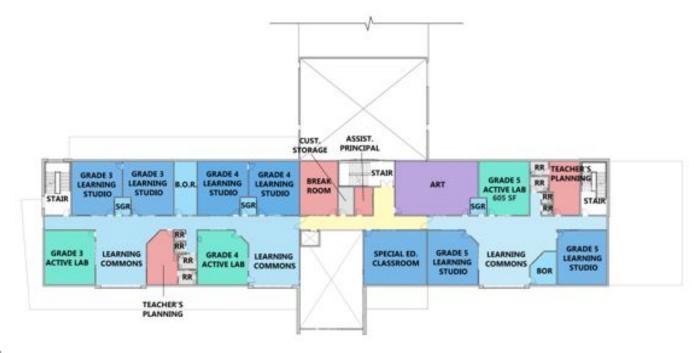

Second Floor

LEGEND

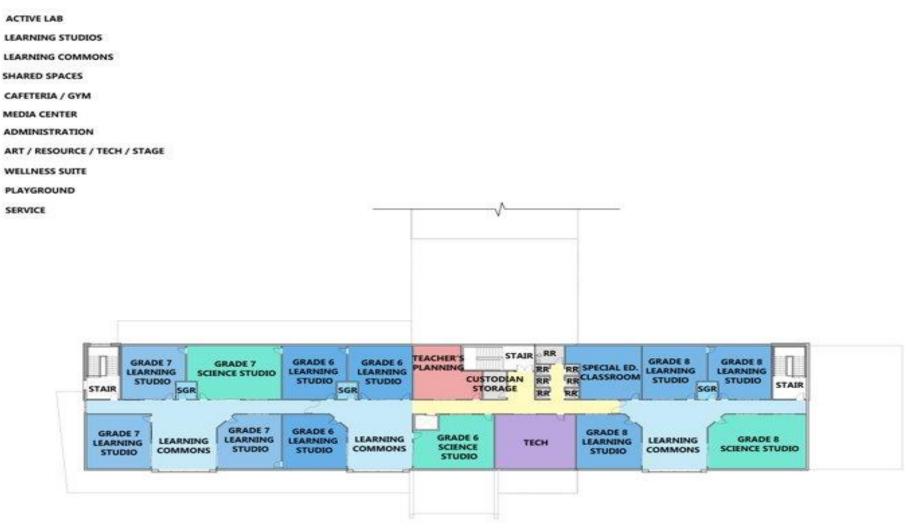

Third Floor





MARY E. FOGARTY ELEMENTARY SCHOOL PRE K - GRADE 5 | 3 TRACK GRADE 6 - GRADE 8 | 4 TRACK




Groundbreakings Fogarty







Classical HS – Renovations

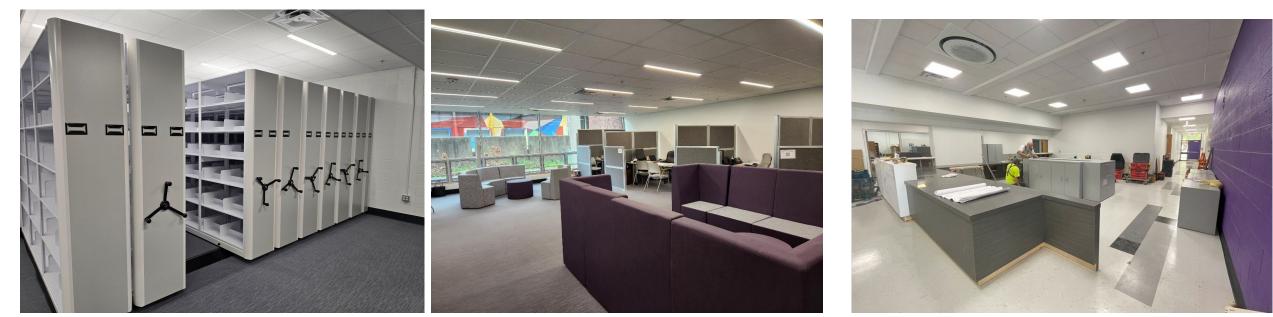

New High Density Shelving Storage

Library Breakout Room

New Admin Furniture



AB


- Administration Office to be completed October 2024
- Construction Complete October 2024
- Lockers and new bookshelves to be delivered by end of 2024
- Move into new Media January 2024

New Kizirian PK-8





New Kizirian PK-8

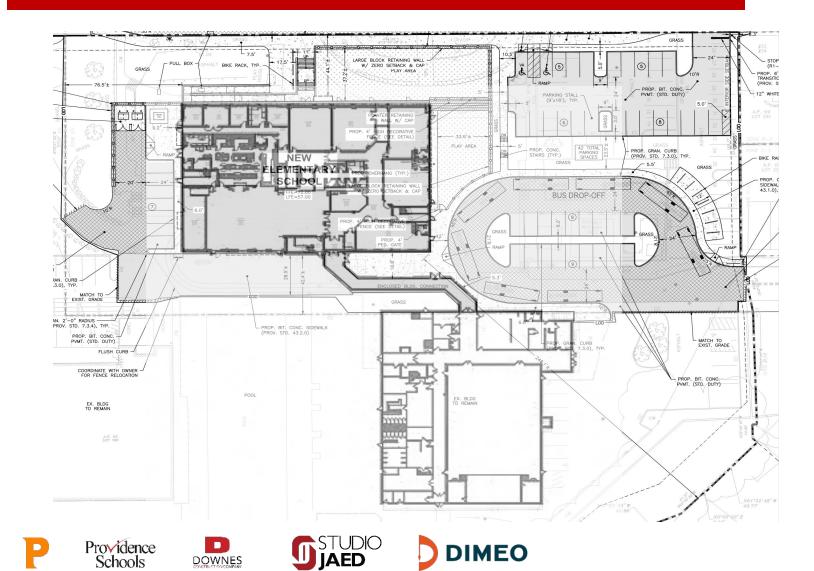

Proceeding with Existing Gym Option Contractor procuring pricing for GMP Project submitted to RIDE portal

Spaziano 6-8 Middle School








100% Construction Documents – Site Plan



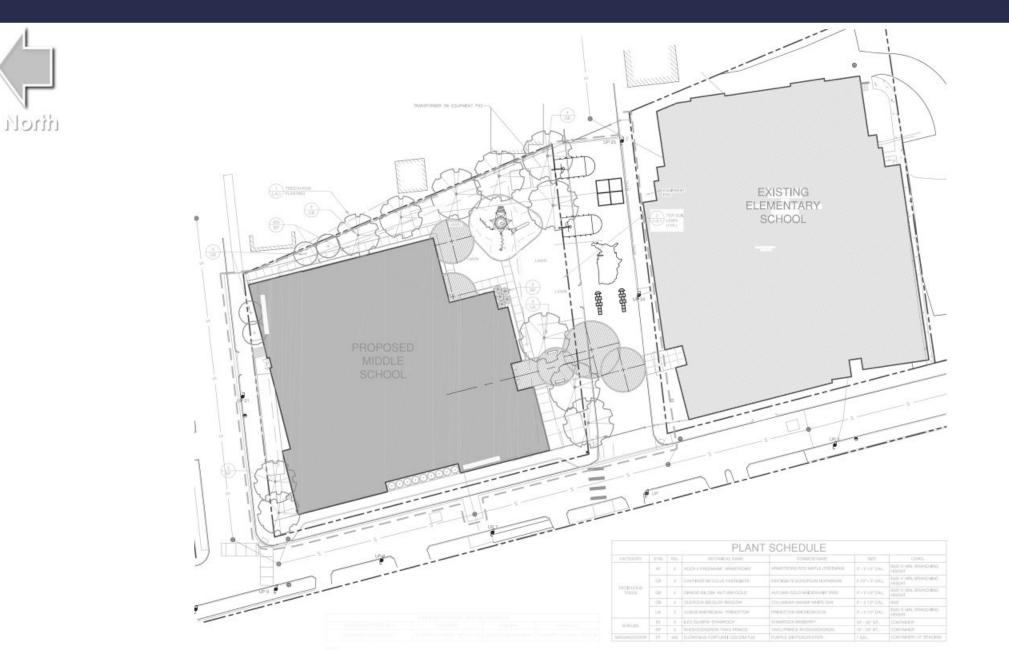

100% CD– Floor Plan Diagrams

0 0

0

0

0

0

0

0

0-


0-

0-

00

OFFICE

n'nol/1

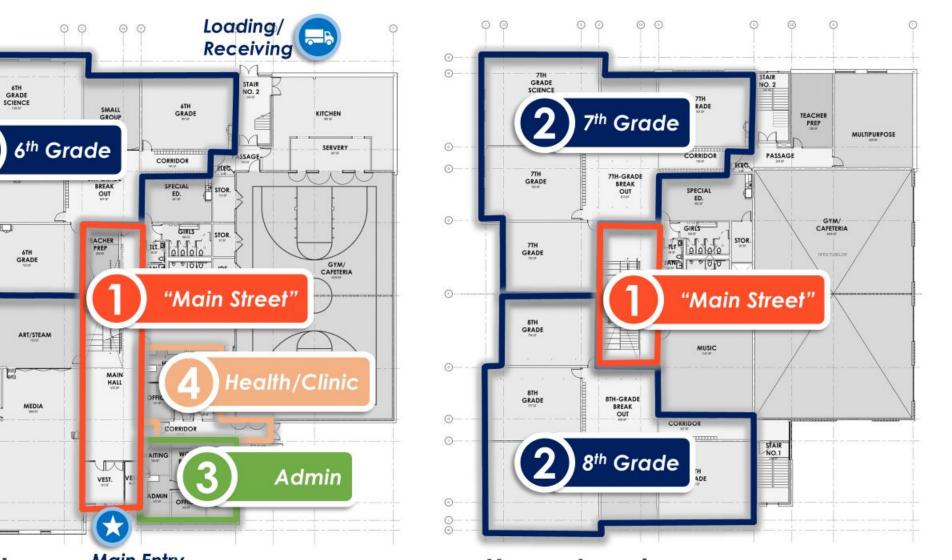

Main Level

Main Entry

Upper Level

Providence Schools

Tecton

ARCHITECTS

APPROVED PLAN MODIFICATIONS



Tecton

ARCHITECTS

thingly





Upper Level

Main Level

UPDATED FLOOR PLANS



Tecton ARCHITECTS



nireli







Upper Level

Groundbreakings Spaziano MS











Mount Pleasant Early College and Career Academy: PLANNING CONCEPT 'A'

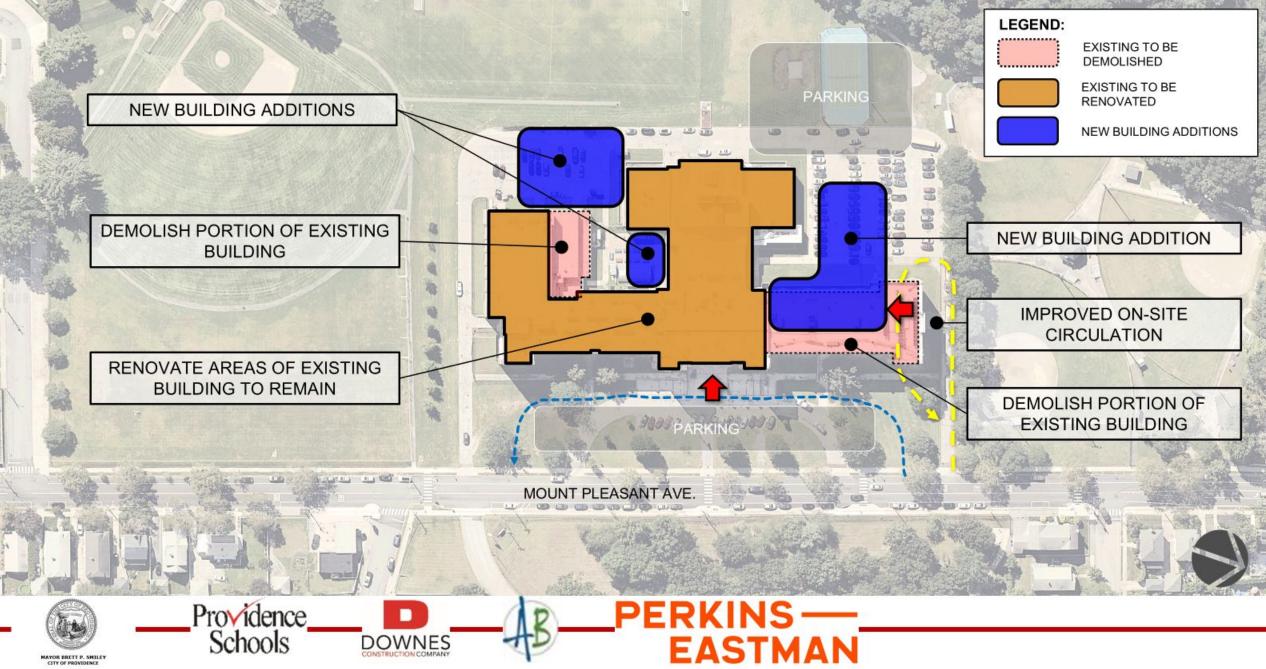

Mount Pleasant Early College and Career Academy: PLANNING CONCEPT 'B'

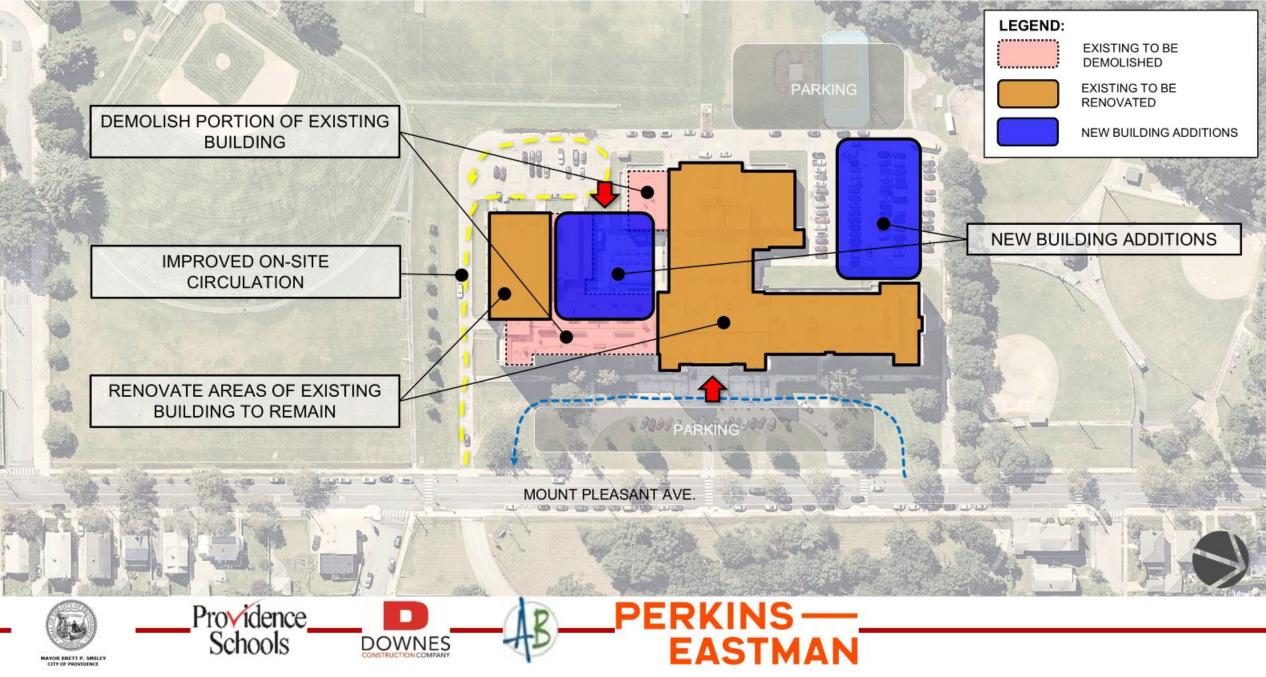

Educational Visioning Workshops





Mount Pleasant Early College and Career Academy Educational Visioning Workshop Overview

Providence Phase 3 School Construction - \$110 Million

To further refine the Mount Pleasant Early College and Career Academy (MPECCA) Stage 2 proposal developed by the Rhode Island Department of Education (RIDE), four Educational Visioning Workshops will be conducted by My Learning Place Integrated Design (MLPID). These workshops will foster collaborative discussions to shape the vision for MPECCA The Mount Pleasant High School community and the School Building Committee (SBC) key stakeholders may include the following:

- Mount Pleasant High School administrators
- Teachers
- Building committee members
- Students
- Parents
- Community partners



Action Item





